



Kent Conservation District
1679 South DuPont Hwy.
Dover, Delaware 19901
stormwater@kentcd.org
(302) 608-5370

APPLICATION FOR STANDARD PLAN APPROVAL
RESIDENTIAL CONSTRUCTION

Disturbance of less than 1 acre

Applicability Criteria

1. The total land disturbance will not exceed 1 acre on any individual lot within the proposed project.
2. The proposed construction is for residential development that does not create common lands, common open space, or a public street.

Site Information

Site Location (911 Address or road name with distance to nearest intersection): _____

Tax Map # _____

Disturbed Acres (nearest 0.1ac): _____

Parcel Total Acres (nearest 0.1ac): _____

Proposed Impervious Area (square feet): _____

Wooded area to be cleared: _____

Applicant Information

Owner: _____

Builder: _____

Mailing Address: _____

Mailing Address: _____

Owner Phone: _____

Builder Phone: _____

Email Address: _____

Email Address: _____

Applicant Certification

I, the undersigned, certify that the information supplied on this Application for Standard Plan Approval is accurate, the proposed land disturbing activity meets the criteria established, and all conditions of this Standard Plan Approval will be met by the applicant, builder, contractor, and owner during construction and post construction.

Applicant Signature: _____ Date: _____

Applicant Printed Name: _____ Title: _____

Fees: \$165.00 for each single family, duplex or townhouse lot. \$85 for a mobile home replacement.

Make checks payable to Kent Conservation District.

NOTE: Final inspection must be requested from the Kent Conservation District prior to issuance of certificate of occupancy. **Allow 2 days for the inspection to be completed.** Inspection requests will not be taken until Stabilization has been completed. An additional fee will be assessed if re-inspection or temporary approval is necessary. Appropriate form and fee must be submitted before temporary approval will be granted.

Approval Information (for office use only)

Permit # _____

Fee Paid: \$ _____

Check # _____

Cash

Expiration Date: _____

Stabilization Conditions

1. Following initial soil disturbance or re-disturbance, temporary or permanent stabilization with seed and mulch shall be completed within 14 calendar days to the surface of all disturbed areas not actively under construction.
2. Specific stabilization recommendations may be found in the Delaware Erosion and Sediment Control Handbook, 3.4.3 Standard and Specifications for Vegetative Stabilization.


Standard Conditions for all Residential Construction

1. Construction site stormwater management best management practices will be used. Standard Detail and Specification DE ESC-3.7.1 ESC for Minor Development will be followed during construction (see attachment).
2. Approval of this Standard Plan does not relieve the applicant from complying with any and all federal, state, county or municipal laws and regulations.

***THIS STANDARD PLAN APPLICATION FORM MUST BE MAINTAINED
ON THE SITE AT ALL TIMES DURING CONSTRUCTION***

Standard Detail & Specifications

ESC for Minor Development

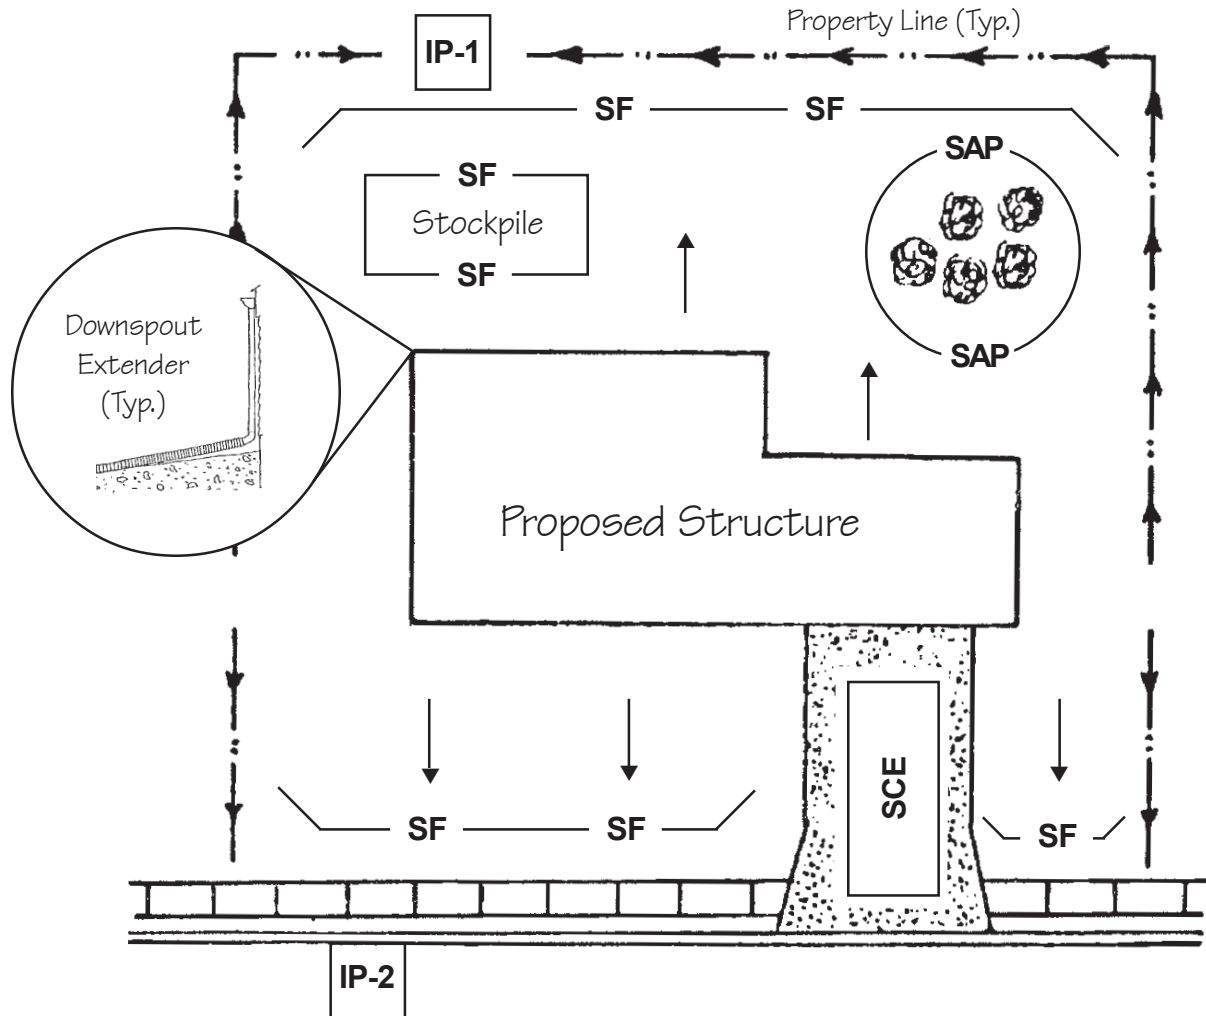

LEGEND

Flow	→	Inlet protection - Type 1	IP-1
Silt Fence	— SF —		
Sensitive Area Protection	— SAP —		
Stabilized Construction Entrance	SCE	Inlet Protection - Type 2	IP-2

Source:

Adapted from IN DNR,
"Erosion Control for the
Home Builder"

Symbol:

Detail No.

DE-ESC-3.7.1

Sheet 1 of 2

Effective July 2023

Standard Detail & Specifications

ESC for Minor Development

Construction Notes:

1. Evaluate the Site.
 - a. Identify Vegetation To Be Saved
 - b. Protect Trees and Sensitive Areas
2. Install Perimeter Erosion And Sediment Controls.
 - a. Protect down-slope areas with vegetative filter strips.
 - b. Protect down-slope areas with silt fence.
 - c. Restrict all lot access to stabilized construction entrance to prevent vehicles from tracking mud onto roadways.
 - d. Install inlet protection on nearby storm drain inlets.
3. Prepare the Site for Construction.
4. Salvage and Stockpile the Topsoil/Subsoil
5. Build the Structure(s) and Install the Utilities.
6. Install Downspout Extenders
7. Maintain the Control Practices.
 - a. Maintain all erosion and sediment control practices until construction is completed and the lot is stabilized.
 - b. Inspect the control practices a minimum of twice a week and after each storm event, making any needed repairs immediately.
8. Revegetate the Building Site.
 - a. Redistribute the stockpiled subsoil and topsoil.
 - b. Seed or sod bare areas.
 - c. Mulch newly seeded areas.
9. Remove Remaining Temporary Control Measures.

Source:

Adapted from IN DNR,
"Erosion Control for the
Home Builder"

Symbol:

Detail No.

DE-ESC-3.7.1

Sheet 2 of 2

Effective July 2023
